



Field Observation Report No. 8 (November)


Date: 11/3/09 - 11/30/09

Project: Bharatiya Temple

Observer: Douglas Necci AIA

Activity Observed:

1. Lower wall masonry complete. Work on masonry parapets progressing, 75% complete.
2. STO gold coat waterproofing 80% complete.
3. Soil erosion issue east of connector noted. Mason's access east wall limited by mud.
4. Wood enclosure of clearstory windows progressing, 80% complete.
5. Roof insulation delivered.
6. Met w/ Ky from Superior to discuss parapet recess for EIFS, 11/5/09.

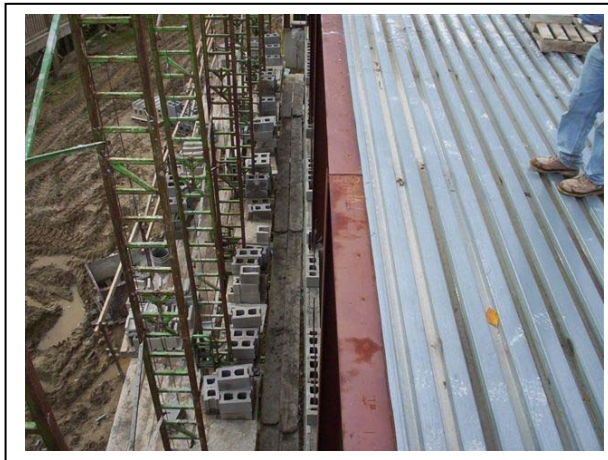

11/3/09



11/3/09



11/5/09



11/5/09



11/12/09



11/12/09



11/13/09



11/13/09



11/13/09



11/30/09
